LEVELOG · CONSTRUCTION PROGRESS REPORT

Harbor Row Tower

Harbor Row, Brooklyn, NY (demo job) · Demo General Contractor

Oct 26 – Nov 8, 2026

Bi-weekly · prepared Nov 9, 2026

High risk

10 / 10	31.8	34	6
Working days with site activity	Average workers on site per day	Peak workforce · Oct 28	Subcontractors on site
	▼ 0.8 vs previous (32.6)		

Overview

6 subcontractors worked on site on 10 of 10 working days, averaging 31.8 workers a day with a peak of 34 on Wed Oct 28. That is in line with the previous period (32.6 a day).

Reported work — Kestrel Concrete: formwork on Top deck; Brightway Electric: conduit on floors 11–13; Northline Mechanical: return ductwork on floors 12–14; Clearspan Glazing: curtain wall panels on floors 8–10.

Regulatory — 2 DOB/DOT violations or complaints open.

Schedule — per the project schedule dated Nov 6, 2026: 20 of 40 scheduled activities complete and forecast finish Sep 13, 2027 against an original Sep 6, 2027.

Progress — concrete in progress; electrical rough-in appears complete on floors 1–7 and 9–12, in progress on floor 13; HVAC / ductwork rough-in appears complete on floors 1–13, in progress on floor 14; sprinklers rough-in appears complete on floors 1–13 (and 1 more kind of work on the progress page), as read from the daily logs.

WORKERS ON SITE



CHANGES SINCE THE PREVIOUS PERIOD

No material change from the previous period.

RISKS AND WATCH ITEMS

- **HIGH** 2 DOB/DOT violations or complaints open: DOB violation DEMO-ECB-0398 and DOB violation DEMO-ECB-0355. R1,R2
- **HIGH** 2 daily inspection items recorded as failed in the daily logs: Fall protection (Nov 6) and Perimeter fence (Oct 30). L
- **WATCH** Permit expiring within 30 days: DOB permit B00DEMO05-S1 (Nov 24, 2026). R3

COMING UP (NEXT 30 DAYS)

- **Tue Nov 24** — DOB permit B00DEMO05-S1 expires [R]
- **Thu Dec 3** — Milestone: Superstructure to floor 20 [S]
- **Fri Dec 4** — Milestone: Permanent power [S]

PROGRESS (ESTIMATED) [L]

Electrical rough-in — **about 55%**

HVAC / ductwork rough-in — **about 60%**

Sprinklers rough-in — **about 60%**

Windows — **about 40%**

Estimated from the filed daily logs; see the progress page.

SCHEDULE [S]

20 of 40 activities complete (count, not a percent)

Finish Sep 13, 2027 vs original Sep 6, 2027 (+7 days)

Per schedule data date Nov 6, 2026

Progress by trade and floor (estimated)

How far each kind of work has got on each floor, read from the filed daily logs up to Nov 8, 2026. Week by week: the estimate at the end of each of the last 12 weeks, read from the logs filed up to that day.

- Concrete (Kestrel Concrete): in progress at Top deck.
- Electrical rough-in (Brightway Electric): appears complete on floors 1–7 and 9–12; in progress on floor 13; started earlier on floor 8; not yet reported on floors 14–22. 11 of 22 floors appear complete, 2 under way.
- HVAC / ductwork rough-in (Northline Mechanical): appears complete on floors 1–13; in progress on floor 14; not yet reported on floors 15–22. 13 of 22 floors appear complete, 1 under way.
- Sprinklers rough-in (Tidewater Fire Protection): appears complete on floors 1–13; not yet reported on floors 14–22. 13 of 22 floors appear complete.
- Windows (Clearspan Glazing): appears complete on floors 1–6 and 8–9; in progress on floor 10; started earlier on floor 7; not yet reported on floors 11–22. 8 of 22 floors appear complete, 2 under way.

KIND OF WORK	ESTIMATE	WEEK BY WEEK	NOT TIED TO A FLOOR
Concrete Kestrel Concrete	not tied to a floor		In progress at Top deck
Electrical rough-in Brightway Electric	about 55%		—
HVAC / ductwork rough-in Northline Mechanical	about 60%		—
Sprinklers rough-in Tidewater Fire Protection	about 60%		—
Windows Clearspan Glazing	about 40%		—

FLOORS 1–22

FLOOR	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22
Electrical rough-in	D	D	D	D	D	D	D	S	D	D	D	D	A	·	·	·	·	·	·	·	·	·
HVAC / ductwork rough-in	D	D	D	D	D	D	D	D	D	D	D	D	D	A	·	·	·	·	·	·	·	·
Sprinklers rough-in	D	D	D	D	D	D	D	D	D	D	D	D	D	·	·	·	·	·	·	·	·	·
Windows	D	D	D	D	D	D	S	D	D	A	·	·	·	·	·	·	·	·	·	·	·	·

D Done — appears complete A Active — worked in the last 7 days S Started — worked earlier · Not reported on that floor

How the estimate is made. Estimated from the filed daily logs: on each floor, work the log reports as complete, or that the next trade in sequence has followed (and the crew has not returned to in a week), counts as complete; work reported on that floor counts as half done; a floor that no log line names for that work counts as not started. Not measured on site and not taken from a schedule. Counted over 22 floors: the 14 a filed daily log has named and 8 more that the confirmed schedule file names (floors 15–22).

Crews on site, day by day G L

Who worked when, and what they reported, from site check-ins and filed daily logs. A bar is days on site, not measured completion.

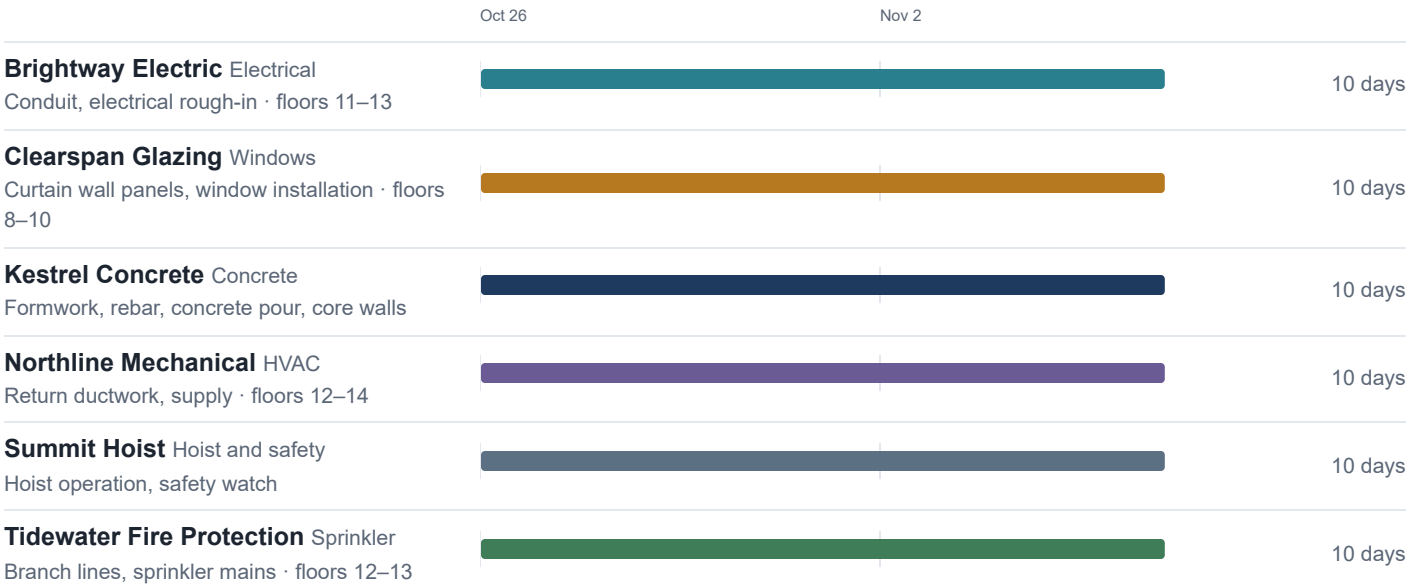

A coloured bar: days on site, in the subcontractor's colour. A weekend between two worked days does not break the bar; a working day with nobody there does.

Schedule and completion S

Per Harbor Row Tower Master Schedule.xlsx, data date Nov 6, 2026, confirmed by Project manager (demo). Completion figures are those the schedule itself reports; Levelog does not estimate completion.

Milestones

MILESTONE	ORIGINAL	CURRENT, OR ACTUAL IF COMPLETE	STATUS
Superstructure to floor 20	Dec 1, 2026	Dec 3, 2026	UPCOMING
Permanent power	Nov 6, 2026	Dec 4, 2026	UPCOMING

Schedule changes shown in the file

ACTIVITY	ORIGINAL	CURRENT	SHIFT
Permanent power	Nov 6	Dec 4	+28 d
Hoist removal	Mar 10	Mar 17	+7 d
Substantial completion	Sep 6	Sep 13	+7 d
Topping out	Dec 10	Dec 17	+7 d

Finish or start dates 7 days or more later than the original; smaller shifts are in the milestone table and the schedule file. Dates as they appear in the schedule file; no cause is inferred.

Scheduled for this period vs. reported

SCHEDULED IN THE SCHEDULE

- Curtain wall floors 1-8 (Sep 15–Nov 10)
- Ductwork floors 9-16 (Oct 6–Dec 3)
- Sprinkler floors 9-16 (Oct 14–Dec 10)
- Concrete floor 15 (Oct 21–Oct 27)
- and 3 more scheduled in this period

REPORTED IN DAILY LOGS

- Kestrel Concrete: Formwork
- Brightway Electric: Conduit
- Northline Mechanical: Return ductwork
- Clearspan Glazing: Curtain wall panels
- Tidewater Fire Protection: Branch lines

- Summit Hoist: Hoist operation

Shown side by side for comparison; the report draws no conclusion from differences in wording.

By floor (activities named for a floor)

FLOOR	1	2	3	4	5	6	7	8	9	10	11	12	13	14
Complete	1 of 1	1 of 1	1 of 1	1 of 1	1 of 1	1 of 1	1 of 1	1 of 1	1 of 1	2 of 2	1 of 1	1 of 1	1 of 1	1 of 1

FLOOR	15	16	17	18	19	20	21	22
Complete	1 of 1	1 of 1	0 of 1	0 of 1	0 of 1	0 of 2	0 of 1	0 of 1

Workforce and site activity G

Workers counted once per day from site check-ins; working days are weekdays, excluding U.S. federal holidays, from the first recorded activity.

SUBCONTRACTOR	TRADE	FLOORS REPORTED	DAYS ON SITE	PREVIOUS	AVG WORKERS	PREVIOUS AVG	PEAK
Kestrel Concrete	Concrete	—	10	9	12.6	13.4	14
Brightway Electric	Electrical	floors 11–13	10	9	4.8	4.9	5
Northline Mechanical	HVAC	floors 12–14	10	9	4.8	4.9	5
Clearspan Glazing	Windows	floors 8–10	10	8	3.8	3.9	4
Tidewater Fire Protection	Sprinkler	floors 12–13	10	9	3.8	3.9	4
Summit Hoist	Hoist and safety	—	10	9	2	2	2

Regulatory and material risks R

DOB/DOT feed checked Nov 9, 2026.

RECORD	NUMBER	ISSUED	STATUS AT PERIOD END	
DOB violation	DEMO-ECB-0398	Oct 20, 2026	OPEN	R1
DOB violation	DEMO-ECB-0355	Sep 2, 2026	OPEN	R2
DOB permit	B00DEMO05-S1	Nov 24, 2025	ISSUED — expires Nov 24, 2026	R3

Listed: records open at the end of the period, records issued or changed during it, and permits that expire within 60 days of its end. A permit in force that expires later is not listed.

Daily site inspections L

50 inspection items were walked on 10 days; 48 passed, 2 failed. Failed: Fall protection (Nov 6), Perimeter fence (Oct 30).

Basis, data notes and evidence

How to read the progress in this report. Documented — work the subs reported in daily logs. **Estimated** — the stages and percentages on the progress page, read from those logs by the fixed rules printed there. **Measurable** — counts or a percent exactly as a confirmed schedule file states them. **Verified physical progress** — not claimed: nothing here is independently verified on site, and no figure is calculated from headcount.

WHAT THIS REPORT DOES NOT CONTAIN

- Progress stages and estimates are read from the filed daily logs by the fixed rules on the progress page. They are not measured or independently verified on site, and no figure is derived from headcount.
- Photographs are supplied in the filed daily logs; their location and date are as filed and are not independently verified.
- Internal GC coordination (messages, reminders, punch-list assignments, free-text site observations) and individual worker information are not included in this report.

DATA NOTES

- Daily logs were filed for 10 of the 10 days with site activity.

Evidence index

ID	SOURCE	DETAIL
G	Site check-ins	318 check-in records, Oct 26–Nov 8 (NFC / QR gate; one worker counts once a day)
L	Filed daily logs	10 daily jobsite logs filed in the period Oct 26 (05d9da), Oct 27 (1931fe), Oct 28 (c7eb14), Oct 29 (0bc046), Oct 30 (ff0a29), Nov 2 (72f31e), Nov 3 (d27a0d), Nov 4 (d1ed22), Nov 5 (d87add), Nov 6 (f4c452)
R1	DOB violation DEMO-ECB-0398	DOB record; status ACTIVE a810-bisweb.nyc.gov
R2	DOB violation DEMO-ECB-0355	DOB record; status ACTIVE a810-bisweb.nyc.gov
R3	DOB permit B00DEMO05-S1	DOB record; status ISSUED a810-bisweb.nyc.gov
S	Project schedule	Harbor Row Tower Master Schedule.xlsx, data date Nov 6, 2026, confirmed by Project manager (demo)

G site check-ins · **L** filed daily logs · **R** DOB/DOT record · **S** project schedule

Generated November 9, 2026 8:00 AM ET · engine 2026.11.2 · reference c7e1b4934d · report demo-biw. The facts printed here are stored with the report.
